



DETECTIVE FOLDER

Schedule of Development Milestones

Resource Schedule

Producer: Young Gou

MS	Deliverables	Date
0	0 - Execution / Pre-Production Deliverables: Documentation & Process • Core GDD / creative vision doc • QA plan / test strategy doc - scope, bug taxonomy, workflow, test-case templates, exit criteria, QA ramp plan • Production Plan / greenlight approval package - consolidates all deliverables below into one approval submission, plus a risk register Legal & Operations • Facility + personnel contracts, signed • Facility/software procurement and licensing Engineering • System framework / tech architecture, initial build - incl. version control/branching strategy and target platform/device range decision • Backend / online scaffolding • Automated test tooling, initial setup Art & Narrative Direction • Visual style bible + directional sketches • Story tone + outline Validation • Playable prototype - Tutorial Level "The Summoner" vertical slice (movement, folding mechanics, camera, level geometry, collectibles, tutorial assembly, case fragment, comic panel presentation)	Oct-30-2026
1	1 - Feature Complete Deliverables: Narrative & Content Production • Narrative outline detail + case content for levels 1-4 • 2 levels (white box + scene concept + character concept); 2 more levels in white box Art & Animation • Base materials + VFX • Main character rig + animation	Apr-30-2027

MS	Deliverables	Date
	Gameplay & Engineering - Cockroach and dinosaur enemy systems - Engineering structure - version control/branching strategy, code architecture module boundaries (gameplay / backend-online / content-pipeline-tools / UI), code review process, basic event-tracking/analytics hooks - Backend performance optimization, ongoing - Internal level toolset - Main feature UI, with multi-device UI adaptation - Automated build pipeline, initial version QA - Detail requirements refinement, automated tooling expansion, narrative/level testing, ongoing Validation - Integrated Alpha build - narrative + gameplay + level + concept art across levels 1-4, reviewed against GDD	
2	2 - Alpha Deliverables: Content Production - Levels 1-4 at Alpha-stage completeness - narrative/level/gameplay/characters/environment/materials/VFX end-to-end playable; not yet audio/voiceover - First live-service version's 2 post-launch levels, white box - One new cosmetic character design Engineering - Monetization/store UI - product display, pricing, purchase entry point - UI / backend / build-pipeline / QA-automation optimization, ongoing; engineering structure: technical debt backlog established and triaged QA - Functional + device compatibility testing on levels 1-4, against the MS0 device matrix Validation - Content Complete build - missing audio/voiceover, reviewed	Jul-30-2027
3	3 - Beta Deliverables: Content Production - Levels 1-4 at true Shippable quality - final polish and bug cleanup - Levels 5-8 at Alpha-stage Audio & Voiceover - Audio - tutorial + levels 1-4 + first 3 months' post-launch content (4 more levels) +	Oct-29-2027


MS	Deliverables	Date
	in-client music • Voiceover - tutorial + levels 1-4 + first 3 months' post-launch content LiveOps & Economy • LiveOps V1 event - first event built from scratch • Economy system - the underlying mechanism/capability for 5 monetization product categories: Battle Pass, Monthly Card, direct currency purchase bundles, direct skin purchase, Starter Pack • Monetization content - the actual character, costume, and decoration assets for the first 3 months' (2 versions) worth of sellable items, distinct from the system above • IAP policy self-check - design-stage review against Apple/Google IAP policies, ahead of the formal MS4 submission QA • Limited closed beta / playtest Marketing • Marketing materials	
4	4 - Certification & Release (RC) Deliverables: Store Submission & Legal • App review submission package - compliance checklist, build, and required documentation for App Store / Google Play • Store listing marketing assets - screenshots, description, icon; distinct from the review submission package above • Legal docs - Privacy Policy (incl. minors'/children's data privacy), Terms of Service / EULA, age/content rating, local/regional regulatory approval • Commercial ops - IAP products configured and live in App Store Connect / Google Play Console Content Production • Levels 5-8, at Shippable Marketing • Marketing campaign Build & QA • Gold Master / RTM build, final and locked • QA full-system final regression pass - levels, monetization, account, UI Live Operations Readiness • Analytics/telemetry dashboards, live and validated; hotfix process ready	Dec-30-2027
5	5 - Archive Deliverables: Source Code & Build Archive • Final GDD, staffing plan, schedule, all style bibles, RTM code - archived as a fully	Jan-14-2028

MS	Deliverables	Date
	version-tagged source repository - Automated tooling - archived (build pipeline config/scripts, QA automation scripts) - Complete build package - archived (iOS + Android builds and debug symbol files) Process & Documentation Archive - Core content-production pipelines - documented (reusable workflows for level, character/skin, event, and battle-pass-season creation); feeds MS6 - QA documentation - archived (QA plan, test case library, known-issues/bug database) - Post-mortem / retrospective document - feeds MS6's template design Legal & Vendor Archive - Review/cert materials, vendor contracts, and legal docs - archived Creative Asset Archive - Art assets - archived in two layers (MS0 directional materials vs. final production assets), organized by Feature ID - Narrative source materials - archived (story bible, full scripts/dialogue) - Audio/VO source files - archived	
6	6 - Live-Service Version Template Staggered/rolling pipeline: 2-3 versions' content in flight simultaneously at different stages, not strictly serial. Deliverables: Content Production (per cycle) 2 levels per cycle - days 1-15 greybox, 15-30 Alpha-stage, 30-45 Shippable - Narrative - case script/dialogue for the 2 levels 1 new character per cycle - modeling/rig/animation 1 new cosmetic skin per cycle - content for the store, distinct from the storefront capability below - Audio/VO - batched every other cycle (~90 days) rather than every cycle LiveOps & Monetization - Monetization storefront - Battle Pass, Monthly Card, direct currency bundles, and direct skin purchase remain available for sale each cycle 1 event per cycle - designed and implemented - Data analysis - prior cycle's retention/monetization data reviewed to inform next cycle's event and economy tuning - A/B testing capability - closes the data-analysis feedback loop QA & Release - QA - regression/certification-style testing pass each cycle - Build/release - packaging and deployment each cycle - Hotfix window - post-release response process each cycle	Template - first cycle begins Jan-2028, repeating every 45 days thereafter

Resource Schedule

Team size across the development phases, aligned to the milestone gates above. Headcount is expressed in full-time equivalents (FTE); the team ramps to a pre-launch peak in Beta, then settles into a sustained live-service crew.

Resource Schedule - Team Size by Phase

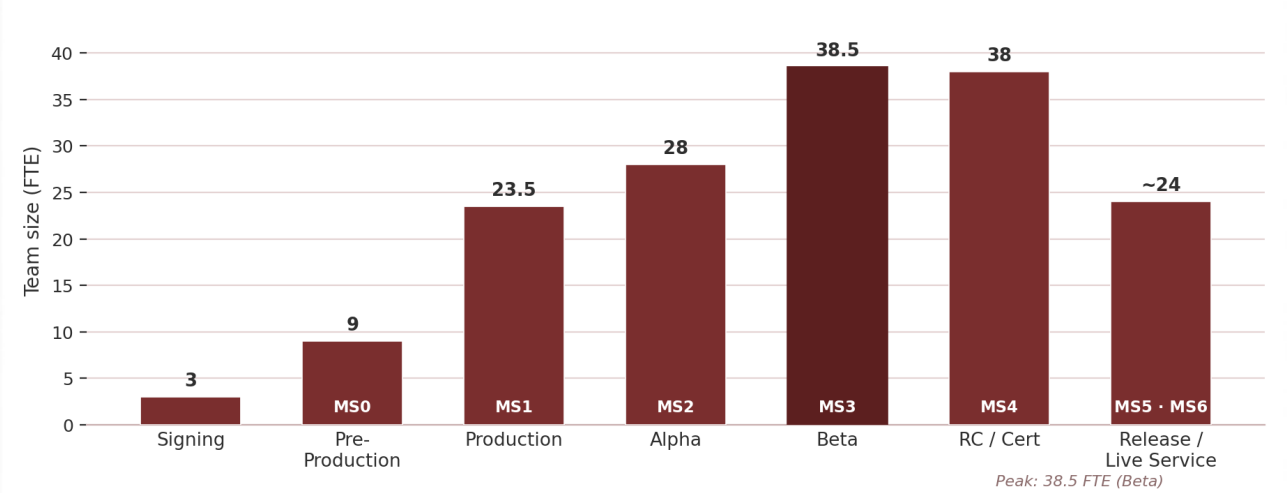

Phase	Timeline	Milestone Gate	Team Size (FTE)
Signing	Jul 2026	-	3
Pre-Production	Aug – Oct 2026	MS0 · Oct 30, 2026	9
Production	Nov 2026 – Apr 2027	MS1 · Apr 30, 2027	23.5
Alpha	May – Jul 2027	MS2 · Jul 30, 2027	28
Beta	Aug – Oct 2027	MS3 · Oct 29, 2027	38.5 (peak)
RC / Certification	Nov – Dec 2027	MS4 · Dec 30, 2027	38
Release / Live Service	Jan 2028 onward	MS5 · Jan 14, 2028 / MS6 template	22 – 27 (steady-state)



End of Milestone Schedule
